



Stagger borrow lengths, widths, and sides of channel along the ditch.

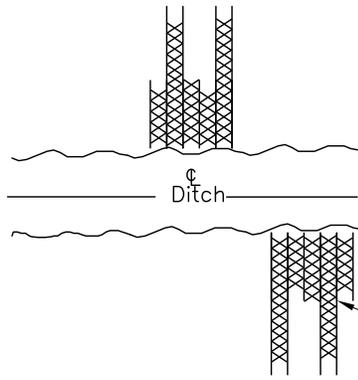

See Sheet _____ for the location of the ditch plugs

Borrow for ditch fill

PLAN VIEW

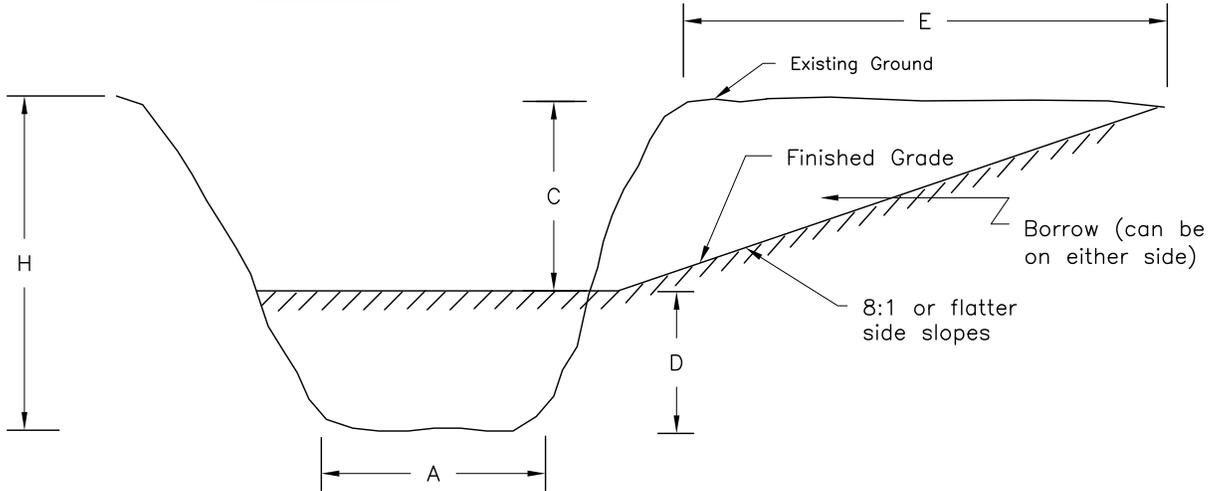

CROSS SECTION

Ditch #	A	C	D	E	H	Length	Cu. Yd.

Total Cu.Yd. _____

Notes:

1. Scrapes/ Borrow areas will be constructed at locations and as flagged by the technician.
2. Wisconsin Construction Specification 2, Excavation, and 3, Earthfill, will be followed.
3. Strip minimum 6" of topsoil and stockpile it for spreading, if needed, after the excavation is completed.
4. Before topsoil is spread, the depth and slopes must be checked by the technician.
5. Seeding shall be done as per Job Sheet 134 for Introduced Species or Job Sheet 135 for Native Species or WI Drawings WI-710 or WI-711.



United States Department of Agriculture

Natural Resources Conservation Service

PARTIAL DITCH FILL

CLIENT: _____
 COUNTY: _____

Date _____
 Designed _____
 Drawn _____
 Checked _____
 Approved _____

File Name
 WI-950D
 Date
 08/14
 Sheet of _____
